




- FSC and of PEFC sourced slow-grown redwood 44mm loglap.
- CE-marked Kerabit high-performance SBS modified roofing shingles (choice of colours)
- 3 x Double glazed, secure, opening windows
- Double glazed, secure door fitted with lever mortice lock
- T&G redwood Timber Floor
- 40mm Board Insulated Roof
- Solar Pipe in roof
- Stained and Preserved
- Delivered and installed by our employees
- 10 Year Manufacturer's Guarantee



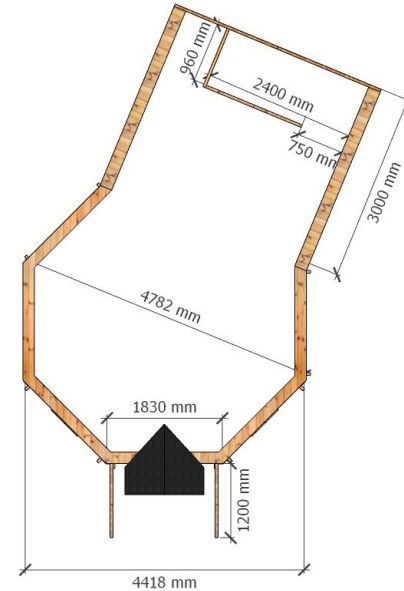

Wall Construction

FSC and of PEFC sourced
slow-grown redwood 44mm loglap.
Pre-treated with exterior stain
preservative.

Floor Construction

16mm timber T&G
25mm Kingspan Insulation
45mm x 45mm 'TANALISED' bearers

Roof Construction

16mm Redwood timber T&G
40mm Kingspan Insulation
12mm T&G internal roof boarding
CE-marked Kerabit high-performance
SBS modified roofing shingles
Solar Pipe

Wooden Doors & Windows

Double glazed opening windows and
Arctic Cabins door with lever mortice
lock

Pegged Base

Composite Timber Posts and
tanalised timber floating base with
25mm of Board Insulation

25mm Board
Insulation added
between joists



Glamping Cabins

1 x extended loglap, insulated roof cabin, with insulated pegged base onto level earth.

Fitted with a solar pipe and 3 double glazed, opening windows per cabin
1.5m Porch
Partition

Included

Delivery and installation to HD9 1XE
Insulated pegged base

Panel carry of 25m from where we park - video required

Excluded

Not including, electrics, plumbing or bathroom fittings

Loglap Cabin	£13,750
En suite partition	£ 500
1.5m Porch	£ 800
Pegged insulated base onto level earth	£ 2,600

Subtotal £ 17,650

Pricing Sale Offer Discounted price £ 16,000

VAT @ 20% £ 3,200

Total inc VAT £ 19,200

Payment Terms

Our payment terms are 20% deposit to secure a space in the calendar and the balance on the final day of installation.

Bank details

Please use your surname as reference

Quality Timber Buildings Ltd

A/C: 33116972

Sort Code 20-63-25
