

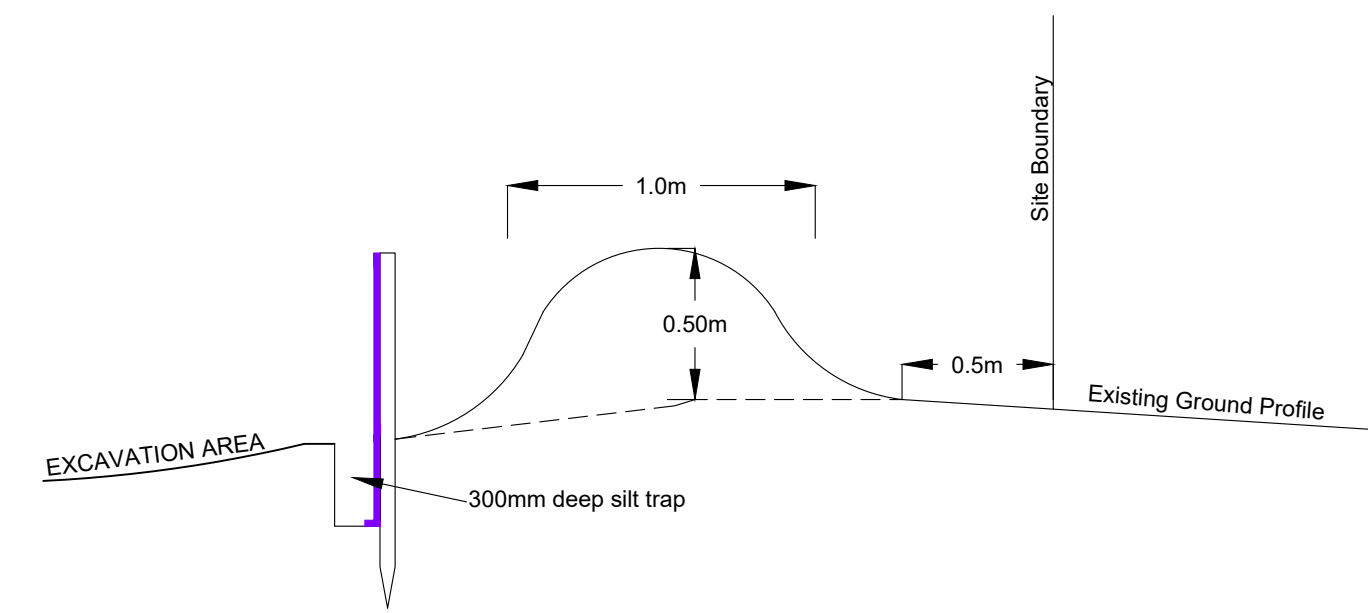
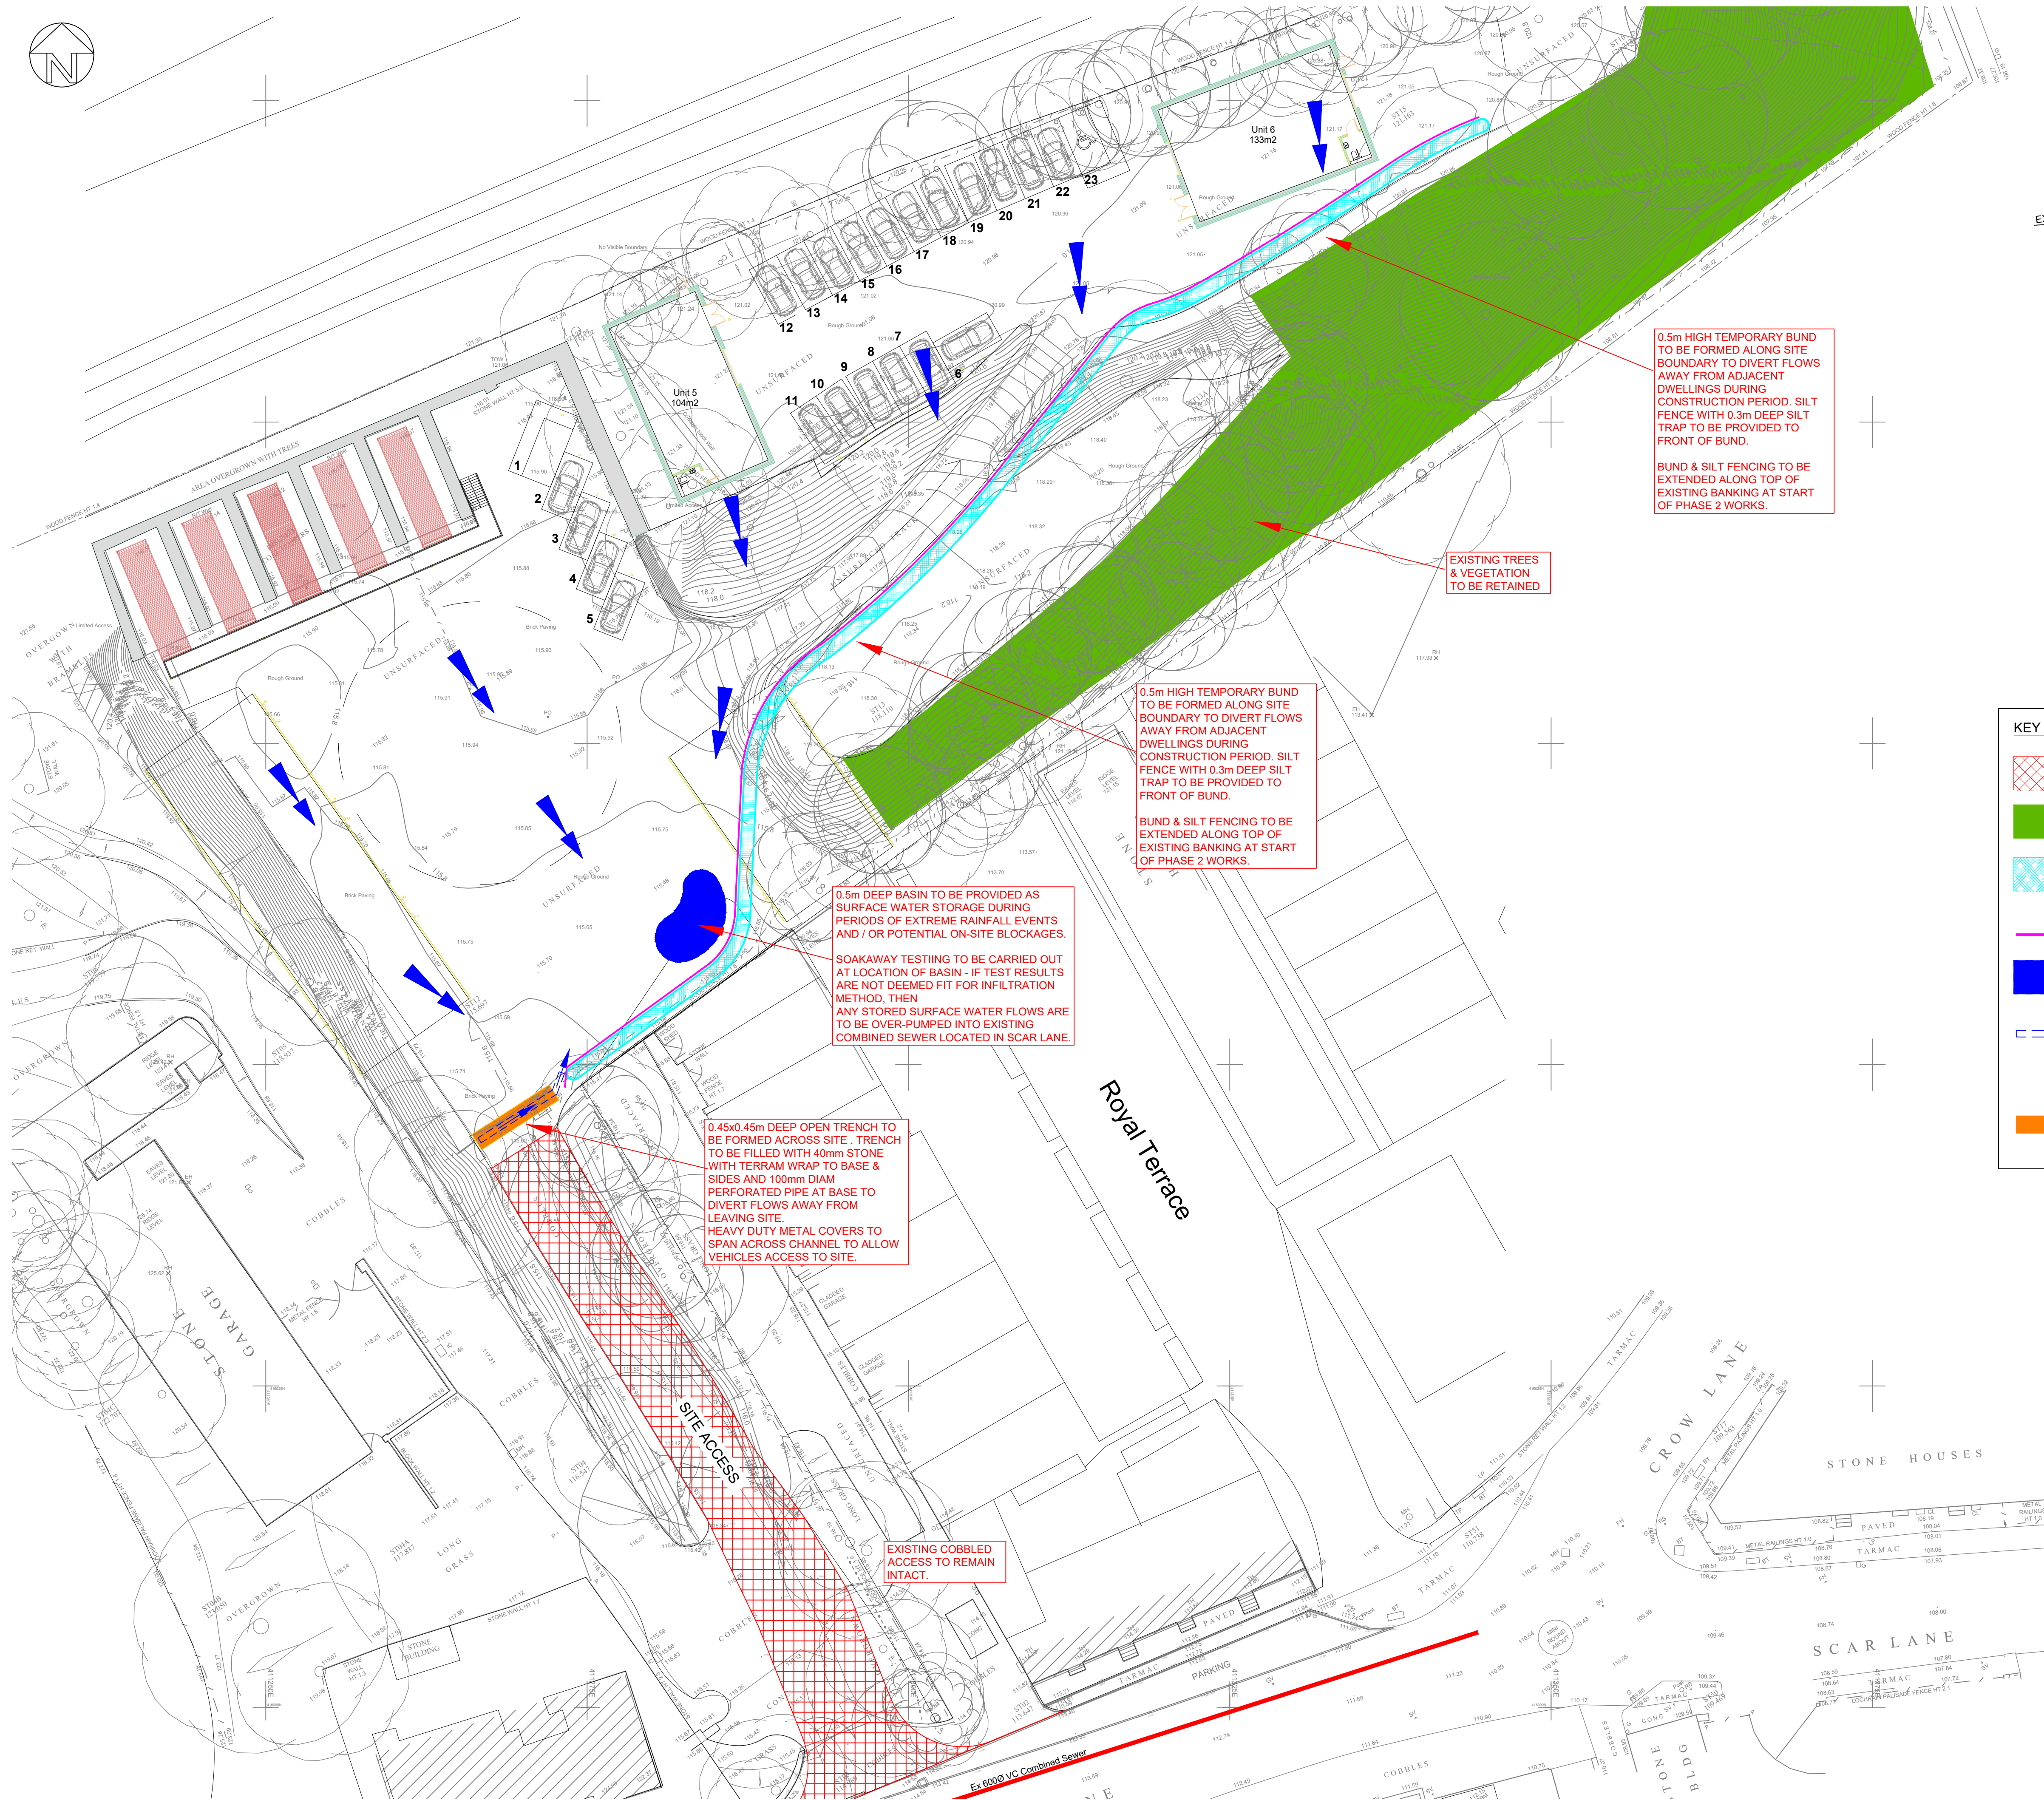




SECTION THRO' TEMPORARY BUND INC SILT FENCE
Scale 1:25

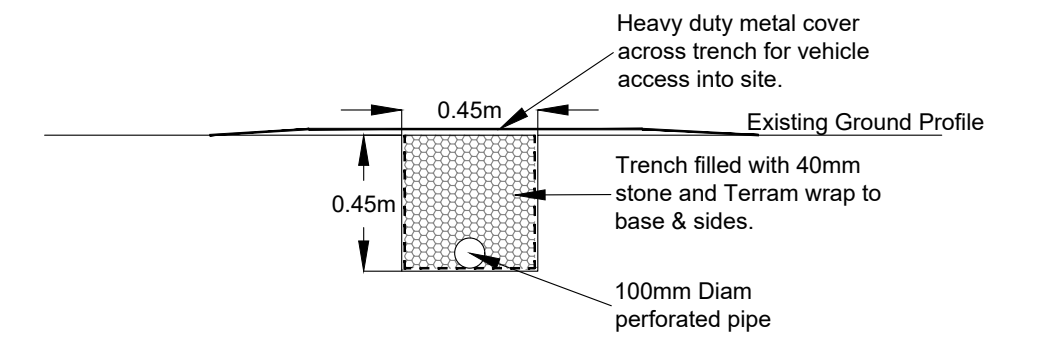

SECTION THRO' TEMPORARY DRAINAGE TRENCH
Scale 1:25

KEY - PHASE 1

- EXISTING SITE ACCESS
- EXISTING VEGETATION TO BE RETAINED
- TEMPORARY BUND TO BE FORMED TO PREVENT FLOWS LEAVING SITE DURING CONSTRUCTION PERIOD. SEE SECTION FOR CONSTRUCTION DETAILS.
- SILT FENCE
- 0.5m DEEP BASIN PROVIDED FOR PERIODS OF EXTREME RAINFALL EVENTS AND / OR POTENTIAL ON-SITE BLOCKAGES
- 0.45x0.45m OPEN TRENCH FILLED WITH 40mm STONE WITH TERRAM WRAP TO BASE & SIDES WITH 100mm DIAM PERFORATED PIPE AT BASE TO DIVERT FLOWS AWAY SITE ACCESS. SEE SECTION FOR CONSTRUCTION DETAILS.
- HEAVY DUTY METAL COVERS TO SPAN ACCESS CHANNEL TO ALLOW VEHICLES TO ACCESS SITE.

SURFACE WATER MANAGEMENT PLAN TO BE RE-ASSESSED BEFORE EACH BUILD PHASE.

MAINTENANCE & INSPECTION TO BE CARRIED OUT:


- ON A WEEKLY BASIS
- FOLLOWING A HEAVY RAINFALL EVENT
- PRIOR TO ANY FORECAST FOR HEAVY RAINFALL

PUMP TO BE PROVIDED ON STAND BY IN CASE OF FAILURE TO TEMPORARY DRAINAGE WORKS AND / OR BASIN- ie. EXCESSIVE SURFACE WATER BUILD UP ON SITE DURING EXTREME STORM EVENTS

EXISTING GULLIES TO BE FILLED WITH SILT SCREENS PROVIDED TO PREVENT SILT TRANSPORTATION. WEEKLY INSPECTION AND MAINTENANCE REQUIRED.

WHEEL WASHING FACILITY TO BE PROVIDED AT SITE ENTRANCE TO PREVENT SILT TRANSPORTATION FROM SITE.

EMERGENCY CONTACT NUMBER TBC



Haigh Huddleston & Associates

Civil Structural Engineering Consultants

Unit 4, Midgley Business Park, Bar Lane, Midgley, Wakefield, WF4 4JJ t 01924 574074

e martin@haighhuddleston.co.uk

Client
BENJAMIN GOOD

Project
SCAR LANE, MILNSBRIDGE

Detail
SURFACE WATER MANAGEMENT PLAN

Dwn	Chkd	Date	Scale	Dwg No.
HH	--	APR 26	1/250 @A1	E25/8392/042
