

Proposed hedge removal to facilitate development

Tree No.	Species	Proposed Works
H1	Crataegus monogyna (Hawthorn),Ilex aquifolium (Holly)	Removal
H6	Crataegus monogyna (Hawthorn),Ilex aquifolium (Holly)	Remove 2m section of hedge for proposed road construction.
H7	Crataegus monogyna (Hawthorn),Ilex aquifolium (Holly)	Remove 2m section of hedge for proposed road construction. Remove 8m section of hedge for proposed swale/boardwalk Remove 10m section of hedge for proposed path and private drive.
H8	Crataegus monogyna (Hawthorn)	Remove 4m section of hedge for proposed path. Remove 2m section of hedge for proposed drainage. Remove section of hedge as required to accommodate scaffold for plot 48.
H9	Crataegus monogyna (Hawthorn),Ilex aquifolium (Holly)	Remove 18m section of hedge for proposed road construction. Remove 8m section of hedge for proposed swale/boardwalk. Remove 2m section of hedge for proposed drainage and footpath.

Total = 1 hedge removed. 4 hedges partially removed.

Proposed tree removal to facilitate development

Tree No.	Species	Proposed Works	Category
T14	Ash	Removal	U
T15	Ash	Removal	U
G5	Alder/Sycamore	Remove one tree as indicated.	C
G9.10	Quercus robur (Common Oak)	Removal	B
G9.11	Tilia cordata (Small-leaved Lime)	Removal	B
G9.12	Prunus avium (Wild Cherry)	Removal	B
G9.13	Tilia cordata (Small-leaved Lime)	Removal	B
G9.17	Quercus robur (Common Oak)	Removal	B
G9.18	Acer pseudoplatanus (Sycamore)	Removal	B
G9.20	Tilia cordata (Small-leaved Lime)	Removal	B
G9.21	Acer pseudoplatanus (Sycamore)	Removal	B
G9.22	Quercus robur (Common Oak)	Removal	B
G9.34	Acer pseudoplatanus (Sycamore)	Removal	C

Total = 13 trees removed.

Proposed tree removal due to poor condition


The following trees are recommended to be felled for management reasons, irrespective of the development proposals. These trees are assessed as Category U, those in poor condition which cannot realistically be retained in the context of the current land use for longer than 10 years.

Tree No.	Species	Proposed Works	Category
G9.4	Prunus avium (Wild Cherry)	Removal	U
G9.19	Prunus avium (Wild Cherry)	Removal	U
G9.24	Prunus avium (Wild Cherry)	Removal	U
G9.39	Prunus avium (Wild Cherry)	Removal	U

Total = 4 trees.

Proposed pruning works to facilitate development

Tree No.	Species	Proposed Works	Category
T41	Malus (Apple)	Prune back to the boundary as required.	C
T42	Fagus sylvatica (Beech)	Prune back to the boundary as required.	C
H5	Crataegus monogyna (Hawthorn),Ilex aquifolium (Holly)	Hard prune as required to facilitate plots 55 to 57.	-
H8	Crataegus monogyna (Hawthorn),Ilex aquifolium (Holly)	Hard prune as required to facilitate construction of plot 48.	-
H9	Crataegus monogyna (Hawthorn),Ilex aquifolium (Holly)	Hard prune to facilitate construction of plots 8, 9 and 11.	-
H10	X Cupressocyparis leylandii (Leyland Cypress)	Prune back to the boundary as required.	-
H11	X Cupressocyparis leylandii (Leyland Cypress)	Prune back to the boundary as required.	-

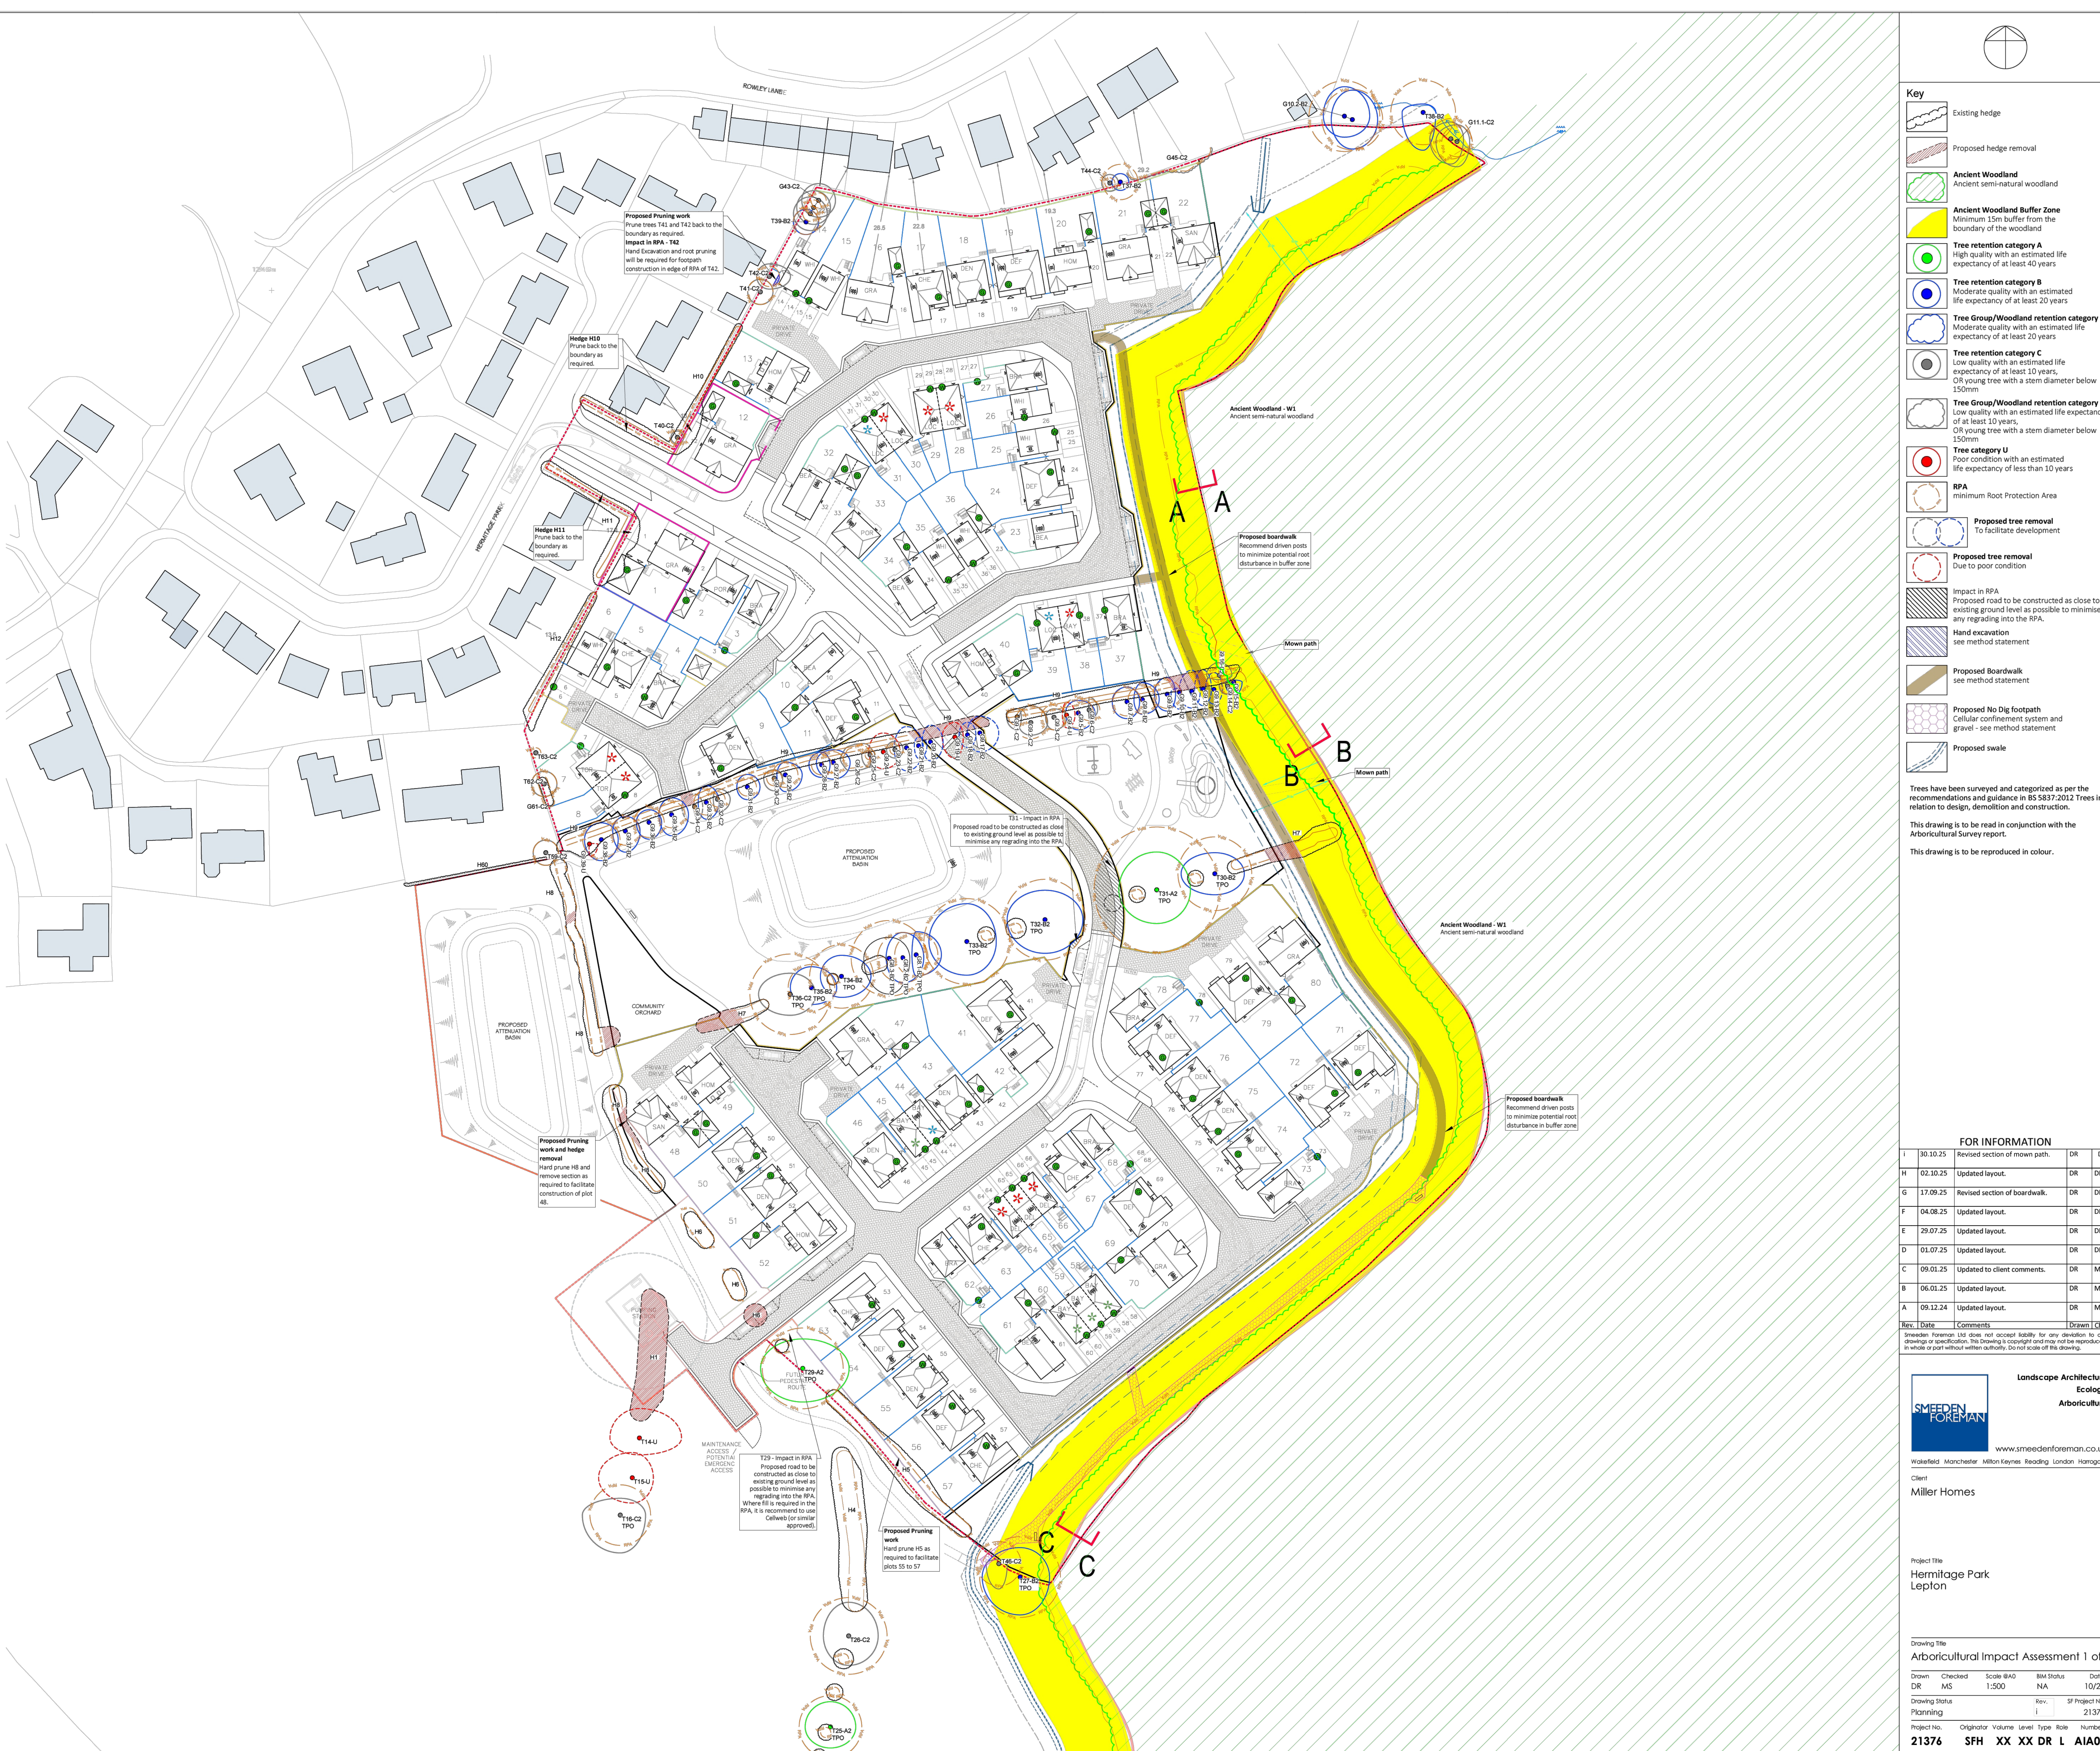

Existing hedge

Proposed hedge removal

Ancient Woodland
Ancient semi-natural woodland

Ancient Woodland Buffer Zone
Minimum 15m buffer from the boundary of the woodland

Tree retention category A
High quality with an estimated life expectancy of at least 40 years

Tree retention category B
Moderate quality with an estimated life expectancy of at least 20 years

Tree Group/Woodland retention category B
Moderate quality with an estimated life expectancy of at least 20 years

Tree retention category C
Low quality with an estimated life expectancy of at least 10 years.
Or young tree with a stem diameter below 150mm

Tree Group/Woodland retention category C
Low quality with an estimated life expectancy of at least 10 years.
Or young tree with a stem diameter below 150mm

Tree category U
Poor condition with an estimated life expectancy of less than 10 years

RPA
minimum Root Protection Area

Proposed tree removal
To facilitate development

Proposed tree removal
Due to poor condition

Impact in RPA
Proposed road to be constructed as close to existing ground level as possible to minimise any regrading into the RPA.

Hand excavation
see method statement

Proposed Boardwalk
see method statement

Proposed No Dig footpath
Cellular confinement system and gravel - see method statement

Proposed swale

Trees have been surveyed and categorised as per the recommendations and guidance in BS 5837:2012 Trees in relation to design, demolition and construction.

This drawing is to be read in conjunction with the Arboricultural Survey report.

This drawing is to be reproduced in colour.

FOR INFORMATION			
I	30.10.25	Revised section of mown path.	DR DR
H	02.10.25	Updated layout.	DR DR
G	17.09.25	Revised section of boardwalk.	DR DR
F	04.08.25	Updated layout.	DR DR
E	29.07.25	Updated layout.	DR DR
D	01.07.25	Updated layout.	DR DR
C	09.01.25	Updated to client comments.	DR MS
B	06.01.25	Updated layout.	DR MS
A	09.12.24	Updated layout.	DR MS
Rev.	Date	Comments	Drawn/Chkd
Smeeden Foreman Ltd does not accept liability for any deviation to our drawing or specification. This drawing is copyright and may not be reproduced in whole or part without written authority. Do not scale off this drawing.			

SMEEDEN FOREMAN

Walsfield Manchester Milton Keynes Reading London Harrogate

Client

Miller Homes

Landscape Architecture

Ecology

Arboriculture

www.smeedenforeman.co.uk

Project Title
Hermitage Park
Lepton

Drawing Title Arboricultural Impact Assessment 1 of 2					
Drawn	Checked	Scale	BM	Status	Date
DR	MS	1:500	NA	NA	10/24
Drawing Status		Rev.	SP Project No		
Planning		I	21376		
Project No.	Originator	Volume	Level	Type	Number
21376	SFH	XX	XX	DR	L AIA01
