FieldTurf®
A Tarkett Sports Company

S&C SLATTER
SPORTS CONSTRUCTION SPECIALISTS

East Bierley

Contract Programme

ID	Task Name	Duration	Start	Finish
1	Contract award	0 days	Mon 05/02/24	Mon 05/02/24
2	Planning	60 days	Mon 10/06/24	Tue 03/09/24
3	FF Panel decision	0 days	Tue 03/09/24	Tue 03/09/24
4	LOI/Signed Contract	0 days	Tue 03/09/24	Tue 03/09/24
5	Mobilisation	21 days	Tue 03/09/24	Tue 14/01/25
6	**Construction start date**	80 days	Mon 20/01/25	Mon 12/05/25
7	Mobilise Site	1 day	Mon 20/01/25	Tue 21/01/25
8	**Car Park works**	0 days	Tue 21/01/25	Tue 21/01/25
9	Site clearence	3 days	Tue 21/01/25	Fri 24/01/25
10	Car park Earthworks	4 days	Fri 24/01/25	Thu 30/01/25
11	Import Car Park stone	5 days	Thu 30/01/25	Thu 06/02/25
12	Car Park kerbs	3 days	Thu 06/02/25	Tue 11/02/25
13	Pitch Earthworks	12 days	Thu 30/01/25	Mon 17/02/25
14	Drainage	7 days	Mon 17/02/25	Wed 26/02/25
15	Inform Labosport of KPI formation and drainage	0 days	Mon 17/02/25	Mon 17/02/25
16	KPI Check Formation and Drainage	0 days	Wed 26/02/25	Wed 26/02/25
17	Retaining wall	7 days	Wed 26/02/25	Fri 07/03/25
18	Install floodlighting bases and ducts	7 days	Fri 07/03/25	Tue 18/03/25
19	Curing for floodlight base concrete	5 days	Tue 18/03/25	Tue 25/03/25
20	Import base stone	10 days	Wed 26/02/25	Wed 12/03/25
21	Lay kerbs	5 days	Wed 12/03/25	Wed 19/03/25
22	Inform Labosport of KPI kerb and Base Check	0 days	Wed 12/03/25	Wed 12/03/25
23	Install macadam base to Pitch and car Park	8 days	Tue 25/03/25	Fri 04/04/25
24	KPI Check kerbs and sub base	0 days	Wed 19/03/25	Wed 19/03/25
25	Install floodlighting columns	5 days	Tue 25/03/25	Tue 01/04/25
26	Install access path and spectator area	10 days	Wed 19/03/25	Wed 02/04/25
27	Mowing strip	10 days	Wed 02/04/25	Wed 16/04/25
28	Macadam surfacing spectator area	5 days	Wed 16/04/25	Wed 23/04/25
29	Install Perimeter Fence	22 days	Wed 19/03/25	Fri 18/04/25
30	Car park surfacing	3 days	Wed 02/04/25	Mon 07/04/25
31	KPI Check Macadam base	0 days	Fri 04/04/25	Fri 04/04/25
32	Install Synthetic Carpet	15 days	Fri 04/04/25	Fri 25/04/25
33	Inform Labosport of Synthetic Turf Check	0 days	Fri 25/04/25	Fri 25/04/25
34	Line Marking	2 days	Fri 25/04/25	Tue 29/04/25
35	KPI Synthetic Turf check	0 days	Tue 29/04/25	Tue 29/04/25
36	Sports equipment	3 days	Tue 29/04/25	Fri 02/05/25
37	Reinstatement	5 days	Fri 02/05/25	Fri 09/05/25
38	KPI Handover Check	0 days	Fri 09/05/25	Fri 09/05/25
39	Build completion	1 day	Fri 09/05/25	Mon 12/05/25
40	Contractor Float	19 days	Tue 15/04/25	Mon 12/05/25
41	**RIBA STAGE 6 HANDOVER**	0 days	Mon 12/05/25	Mon 12/05/25

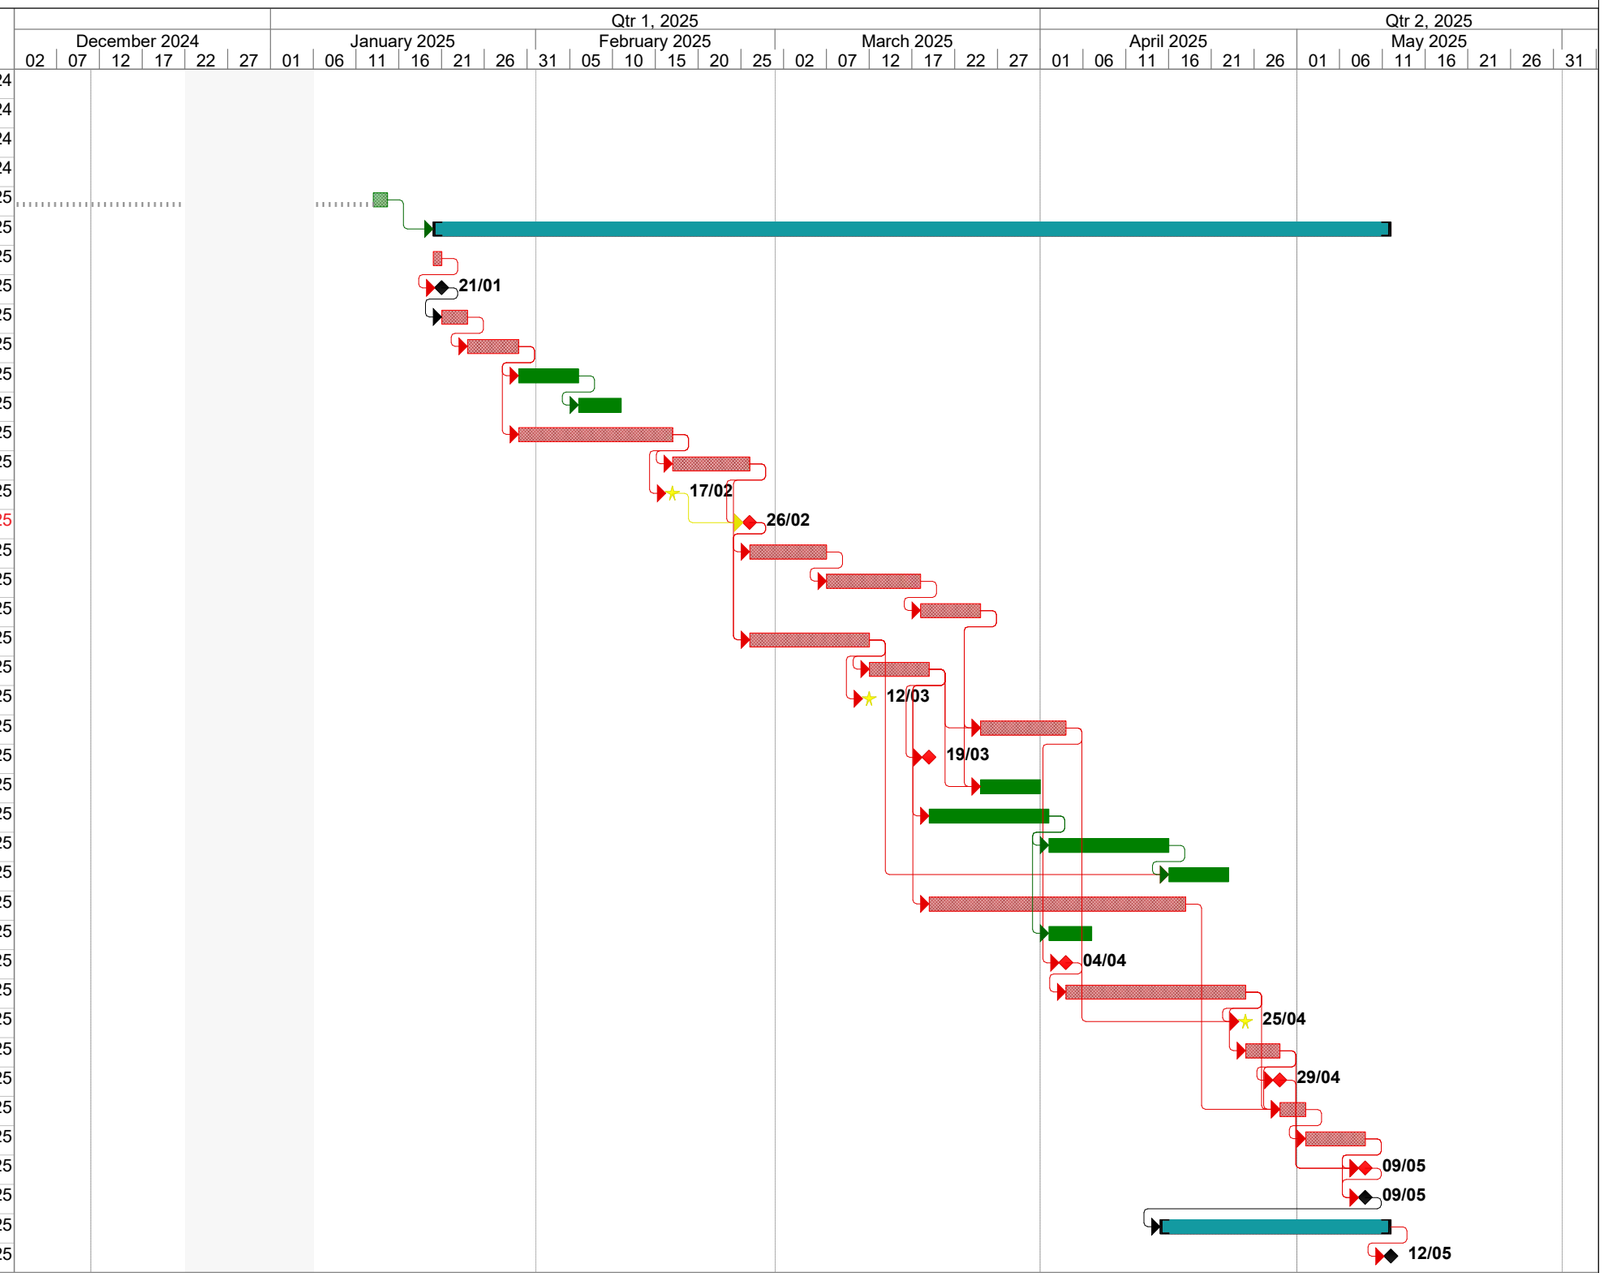

East Birerley Contract Programme
Wed 11/12/24

Task		Rolled Up Critical Task		Project Summary		Inactive Summary		Start-only	
Critical Task		Rolled Up Milestone		Group By Summary		Manual Task		Finish-only	
Milestone		Rolled Up Progress		Inactive Task		Duration-only		Progress	
Summary		Split		Inactive Task		Manual Summary Rollup		Deadline	
Rolled Up Task		External Tasks		Inactive Milestone		Manual Summary			
