
Cummins Huddersfield Footbridge - Construction Programme Rev4


Activity ID	Activity Name	Original Duration	Start	Finish
Cummins Huddersfield Footbridge - Construction Programme Rev4		481.000	21-Nov-24 17:00 A	22-Oct-26 17:00
A1020	Contract award	21.000	14-Jan-25 08:00 A	11-Feb-25 17:00 A
A1780	Letter of intent	0.000	14-Jan-25 08:00 A	
A1010	Tender review period	24.000	22-Nov-24 08:00 A	02-Jan-25 17:00 A
A1000	Tender submission	0.000		21-Nov-24 17:00 A
Pre-Construction Phase		311.000	14-Jan-25 08:00 A	07-Apr-26 17:00
Design		224.000	14-Jan-25 08:00 A	28-Nov-25 17:00
RIBA Stage 4		224.000	14-Jan-25 08:00 A	28-Nov-25 17:00
A1360	AFC drawings Issued	0.000		28-Nov-25 17:00
A1190	Appoint Civils Designer	0.000	14-Jan-25 08:00 A	
A1260	Architectural detailing	60.000	31-Jan-25 08:00 A	23-May-25 17:00 A
A1331	Cat 2 Check Design/Cat 3 CFD Checks	77.000	06-Aug-25 08:00	21-Nov-25 17:00
A1200	Civils and Structural Design	73.000	14-Jan-25 08:00 A	23-May-25 17:00 A
A1250	Comms Systems Design (M&E)	60.000	31-Jan-25 08:00 A	12-Jun-25 08:00 A
A1330	Design approval period (Post DRN)	20.000	06-Aug-25 08:00	03-Sep-25 17:00
A1340	Design approved by client and technical approval authority	0.000		21-Nov-25 17:00
A1300	Design review period in highways approval and revised planning permission	40.000	27-May-25 08:00 A	22-Jul-25 17:00
A1350	Designer Produces AFC drawings	5.000	24-Nov-25 08:00	28-Nov-25 17:00
A1240	Fire Alarm System design (M&E)	60.000	31-Jan-25 08:00 A	12-Jun-25 08:00 A
A1230	HVAC Design (M&E)	60.000	31-Jan-25 08:00 A	12-Jun-25 08:00 A
A1310	Issue design review comments (DRN)	0.000		22-Jul-25 17:00
A1280	Lift design (Specialist designer)	60.000	31-Jan-25 08:00 A	12-Jun-25 08:00 A
A1270	Lightning Conductor Design (M&E)	60.000	31-Jan-25 08:00 A	12-Jun-25 08:00 A
A1220	M&E Design (M&E)	60.000	31-Jan-25 08:00 A	12-Jun-25 08:00 A
A1320	Respond to DRN	10.000	23-Jul-25 08:00	05-Aug-25 17:00
A1301	Road Safety Stage 1&2 Audit	10.000	12-Jun-25 08:00*	25-Jun-25 17:00
A1302	Road Safety Stage 1&2 Audit Review	40.000	26-Jun-25 08:00	20-Aug-25 17:00
A1210	Site investigation	20.000	28-Mar-25 08:00 A	16-Apr-25 17:00 A
A1290	Submit Design to Client and Technical approval authority	0.000		23-May-25 08:00 A
Revised Planning Application		40.000	14-Mar-25 08:00 A	25-Mar-25 17:00 A
A1830	Planning application approval period	40.000	14-Mar-25 08:00 A	25-Mar-25 17:00 A
A1840	Planning Application approved	0.000		25-Mar-25 17:00 A
A1820	Revised planning application submission	0.000		14-Mar-25 08:00 A
Re-Price following design		53.000	27-May-25 08:00 A	11-Aug-25 17:00
A1800	CML/Cummins Price confirmation/agreement	23.000	10-Jul-25 08:00	11-Aug-25 17:00
A1370	Confirm fixed price for Construction Phase	30.000	27-May-25 08:00 A	09-Jul-25 17:00
A1810	Final Contract agreement	5.000	05-Aug-25 08:00	11-Aug-25 17:00
Procurement		203.000	17-Jun-25 08:00	01-Apr-26 17:00
A1850	Bridge Fabrication	65.000	31-Dec-25 08:00	01-Apr-26 17:00
A1790	Bridge Fabrication Drawings	25.000	24-Nov-25 08:00	30-Dec-25 17:00
A1860	Lead time for lift (inc Design)	130.000	12-Aug-25 08:00	13-Feb-26 17:00
A1770	Piling Design	40.000	17-Jun-25 08:00	11-Aug-25 17:00
A2080	Supply Chain contracts and procurement	33.000	12-Aug-25 08:00	26-Sep-25 17:00
CDM Documentation		165.000	12-Aug-25 08:00	07-Apr-26 17:00
Construction Phase Plan		30.000	12-Aug-25 08:00	23-Sep-25 17:00
A2120	CPP Approved	0.000		23-Sep-25 17:00
A2110	CPP Review Period	20.000	27-Aug-25 08:00	23-Sep-25 17:00
A2090	Produce Construction Phase Plan	10.000	12-Aug-25 08:00	26-Aug-25 17:00
A2100	Submit CPP to client/CDM planner	0.000		26-Aug-25 17:00
RAMS		102.000	10-Nov-25 08:00	07-Apr-26 17:00
RAMS001 - Site Setup and Establishment		20.000	10-Nov-25 08:00	05-Dec-25 17:00
A2130	Produce RAMS001	10.000	10-Nov-25 08:00	21-Nov-25 17:00
A2160	RAMS001 Approved	0.000		05-Dec-25 17:00
A2150	RAMS001 Review Period	10.000	24-Nov-25 08:00	05-Dec-25 17:00
A2140	Submit RAMS001 to client/CDM planner	0.000		21-Nov-25 17:00
RAMS002 - Groundworks and Piling		30.000	19-Nov-25 08:00	02-Jan-26 17:00
A2180	Produce RAMS002	10.000	19-Nov-25 08:00	02-Dec-25 17:00
A2210	RAMS002 Approved	0.000		02-Jan-26 17:00
A2200	RAMS002 Review Period	20.000	03-Dec-25 08:00	02-Jan-26 17:00
A2190	Submit RAMS002 to client/CDM planner	0.000		02-Dec-25 17:00
RAMS003 - Steel Erection East and West Towers		30.000	05-Jan-26 08:00	13-Feb-26 17:00
A2220	Produce RAMS003	10.000	05-Jan-26 08:00	16-Jan-26 17:00
A2250	RAMS003 Approved	0.000		13-Feb-26 17:00
A2240	RAMS003 Review Period	20.000	19-Jan-26 08:00	13-Feb-26 17:00
A2230	Submit RAMS003 to client/CDM planner	0.000		16-Jan-26 17:00
RAMS004 - Installation of Main Span		35.000	16-Feb-26 08:00	07-Apr-26 17:00
A2260	Produce RAMS004	10.000	16-Feb-26 08:00	27-Feb-26 17:00
A2290	RAMS004 Approved	0.000		07-Apr-26 17:00
A2280	RAMS004 Review Period	20.000	09-Mar-26 08:00	07-Apr-26 17:00
A2270	Submit RAMS004 to client/CDM planner	0.000		06-Mar-26 17:00
RIBA Stage 5 - Construction Phase		176.000	08-Dec-25 08:00	19-Aug-26 17:00
Site Mobilisation		10.000	08-Dec-25 08:00	19-Dec-25 17:00
A1040	Site setup and mobilisation	10.000	08-Dec-25 08:00	19-Dec-25 17:00
A1030	Start on Site	0.000	08-Dec-25 08:00*	
Substructure		40.000	05-Jan-26 08:00	01-Mar-26 16:00
East Foundation		30.000	05-Jan-26 08:00	15-Feb-26 17:00
A1050	CFA piling to east side (landscaped area) 6 per day	5.000	12-Jan-26 08:00	16-Jan-26 17:00
A1110	East pile cap curing period	7.000	09-Feb-26 08:00	15-Feb-26 17:00
A1070	East side piles curing time	7.000	19-Jan-26 08:00	25-Jan-26 17:00
A1870	Install piling mat to East Side	5.000	05-Jan-26 08:00	09-Jan-26 17:00
A1090	Shutter and pour east pile cap	10.000	26-Jan-26 08:00	06-Feb-26 17:00
West Foundation		28.000	21-Jan-26 08:00	01-Mar-26 16:00
A1060	CFA piling to west side (building connection) 9no	3.000	28-Jan-26 08:00	30-Jan-26 17:00
A1880	Install piling mat to West side	5.000	21-Jan-26 08:00	27-Jan-26 17:00
A1100	Shutter and pour west side pile cap	10.000	09-Feb-26 08:00	20-Feb-26 17:00
A1120	West pile cap curing period	7.000	23-Feb-26 08:00	01-Mar-26 16:00
A1080	West side piles curing time	7.000	02-Feb-26 08:00	08-Feb-26 16:00
Superstructure		37.000	16-Feb-26 08:00	09-Apr-26 17:00
Lift Shaft		5.000	02-Mar-26 08:00	06-Mar-26 17:00
A1160	Construct eastern blockwork lift shaft	5.000	02-Mar-26 08:00	06-Mar-26 17:00
Frame		36.000	16-Feb-26 08:00	08-Apr-26 17:00
A1130	Assemble eastern frame and staircases using crane (daytime)	10.000	16-Feb-26 08:00	27-Feb-26 17:00
A1410	Assemble western frame and staircase using crane	10.000	02-Mar-26 08:00	13-Mar-26 17:00
A1890	Install main span, full road closure	1.000	08-Apr-26 08:00	08-Apr-26 17:00
External Walls		17.000	16-Mar-26 08:00	09-Apr-26 17:00
A1390	Install external wall and cladding to eastern frame and western Frame	15.000	16-Mar-26 08:00	07-Apr-26 17:00

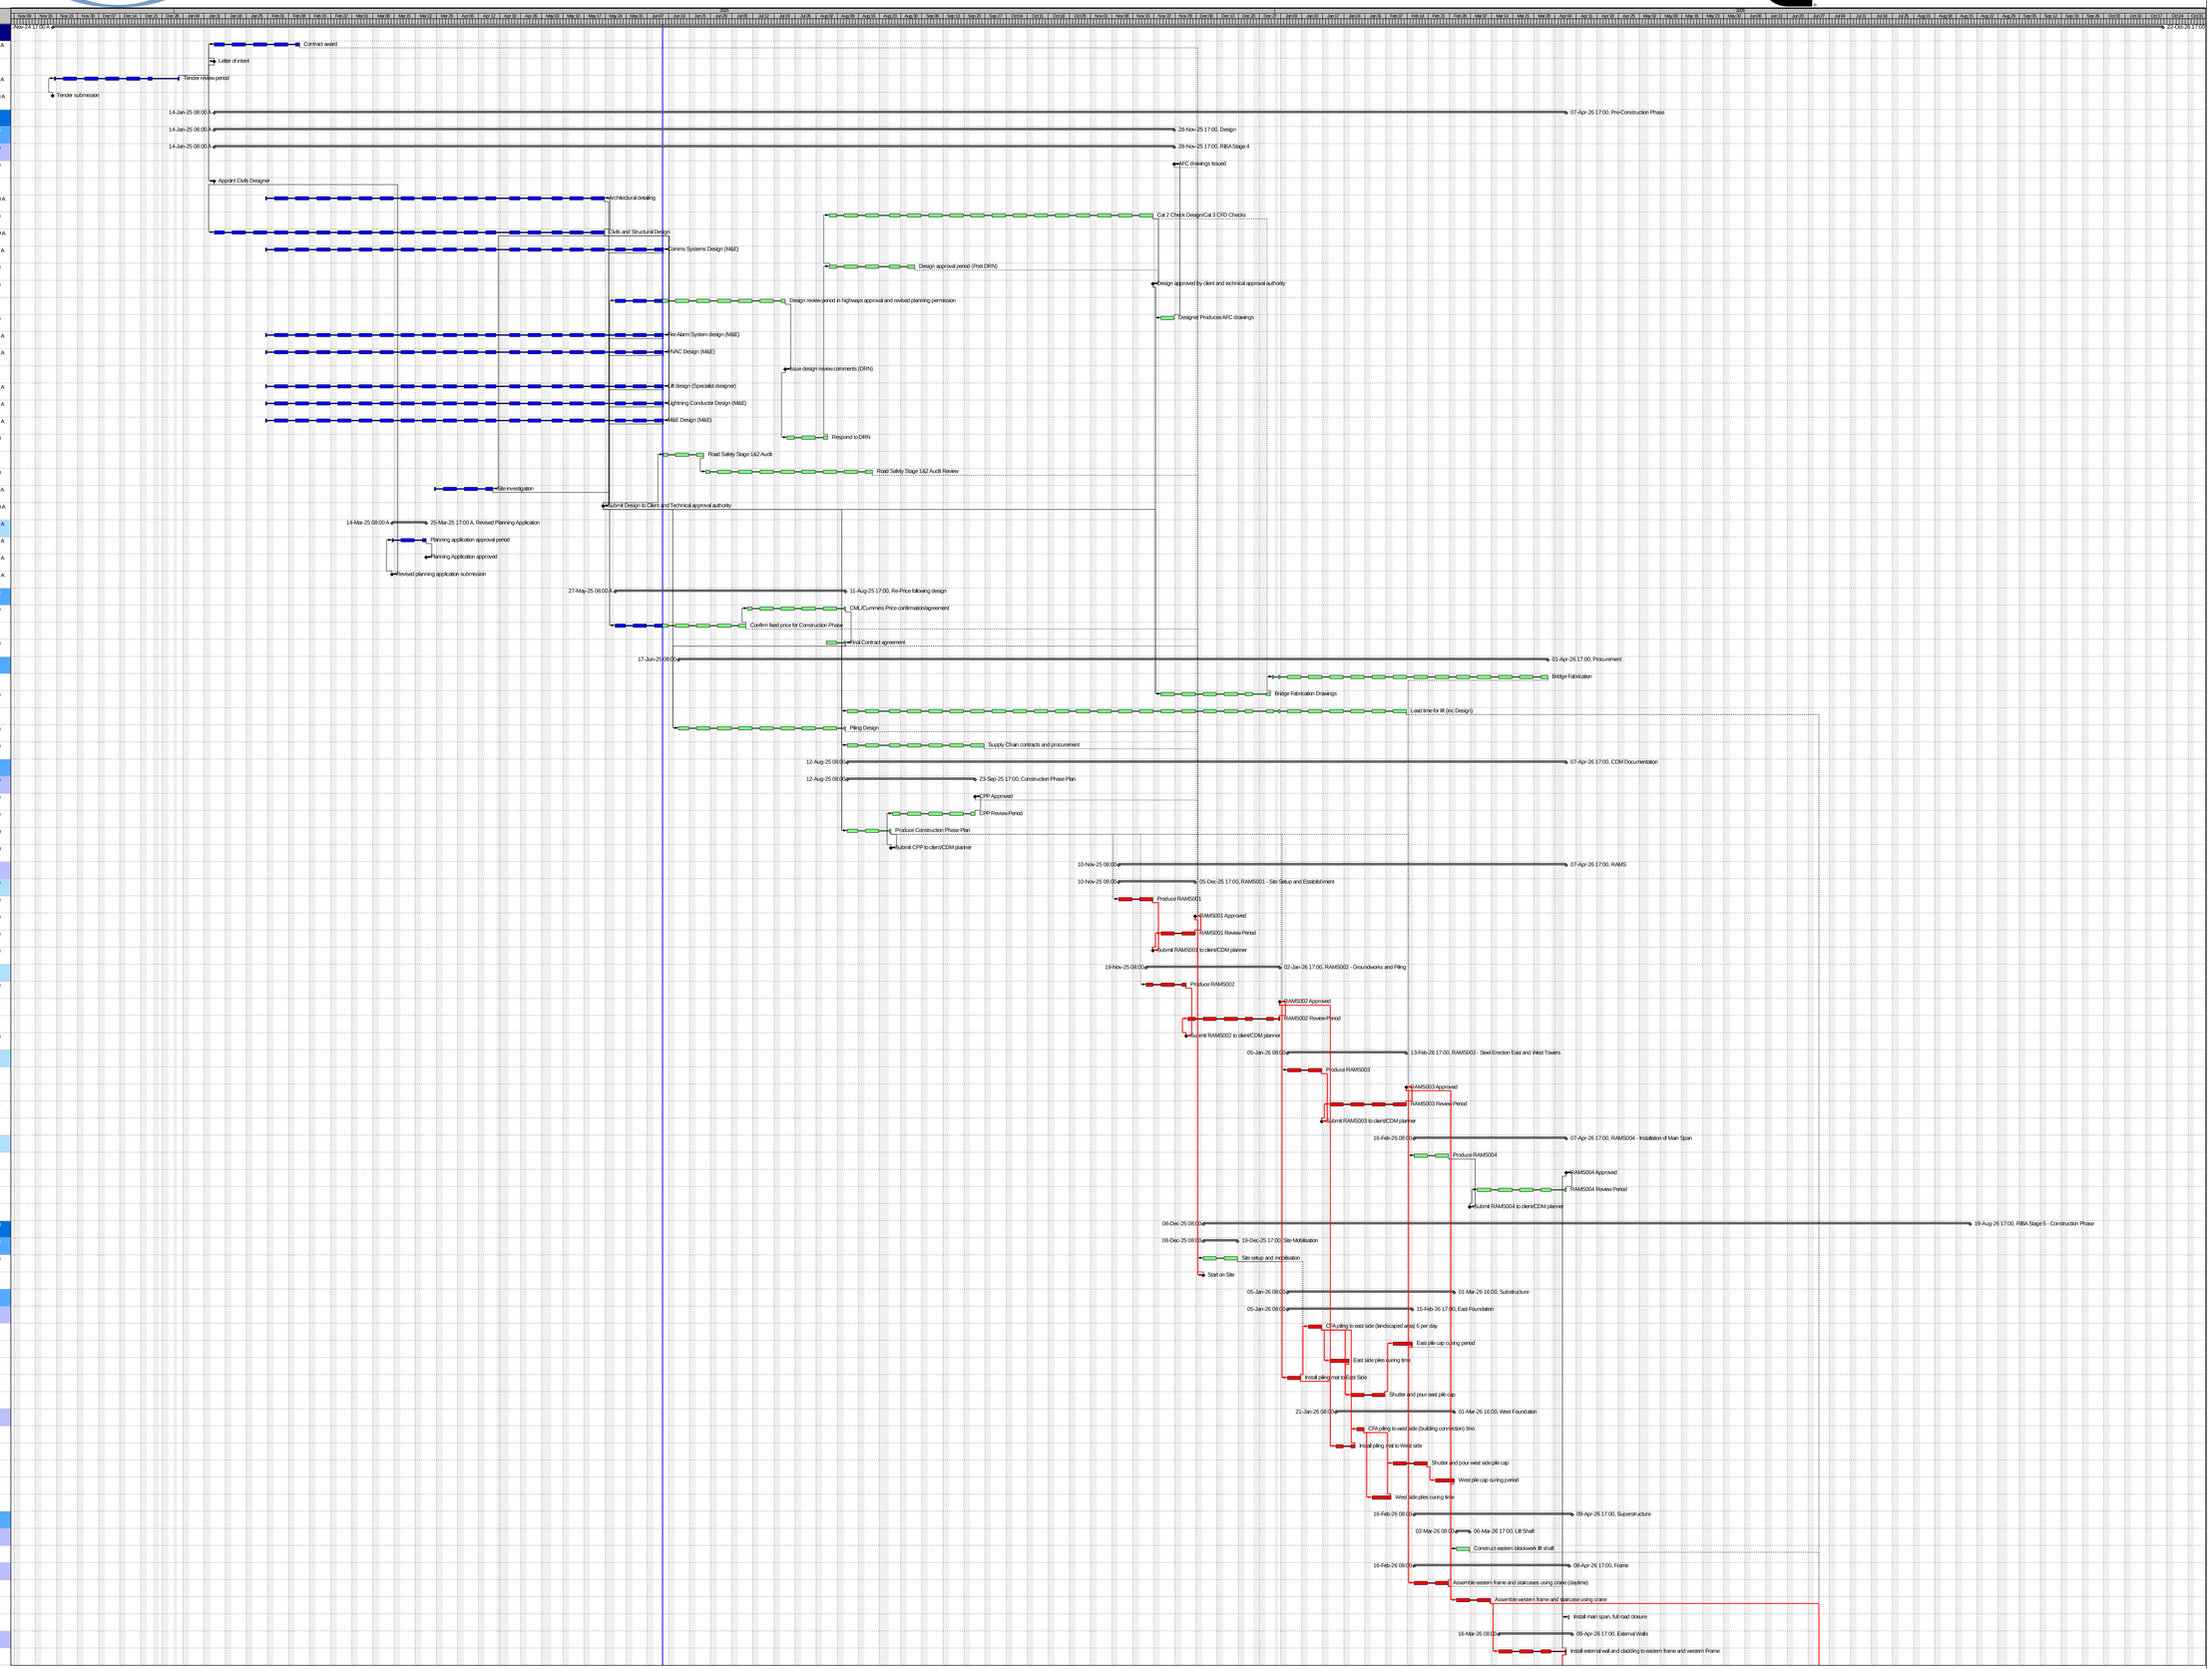

© Oracle Corporation

Cummins Huddersfield Footbridge - Construction Programme Rev4

Activity ID	Activity Name	Original Duration	Start	Finish
A1400	Install Illuminated sign (Fixing only)	2.00d	08-Apr-26 08:00	09-Apr-26 17:00
Internal Finishes		47.00d	08-Apr-26 08:00	15-Jun-26 17:00
Floor Finishes		10.00d	08-Apr-26 08:00	21-Apr-26 17:00
A1440	Install stairs and internal floors (finishing) (Upper Ground Floor / Second Floor (Bridge Level) both	10.00d	08-Apr-26 08:00	21-Apr-26 17:00
Internal Walls and Partitions		15.00d	20-Apr-26 08:00	11-May-26 17:00
A1560	Install internal walls	15.00d	20-Apr-26 08:00	11-May-26 17:00
Internal Doors		15.00d	11-May-26 08:00	01-Jun-26 17:00
A1570	Install internal doors and ironmongery	15.00d	11-May-26 08:00	01-Jun-26 17:00
Wall Finishes		10.00d	02-Jun-26 08:00	15-Jun-26 17:00
A1650	Internal Wall Finishing	10.00d	02-Jun-26 08:00	15-Jun-26 17:00
Ceiling Finishes		10.00d	02-Jun-26 08:00	15-Jun-26 17:00
A1680	Internal ceiling finishing	10.00d	02-Jun-26 08:00	15-Jun-26 17:00
Services		59.00d	22-Apr-26 08:00	15-Jul-26 17:00
First Fix		27.00d	22-Apr-26 08:00	01-Jun-26 17:00
Electrical		13.00d	22-Apr-26 08:00	11-May-26 17:00
A1940	First Fix Testing	1.00d	11-May-26 08:00	11-May-26 17:00
A1900	Install Cable Trunking	5.00d	22-Apr-26 08:00	28-Apr-26 17:00
A1910	Install Conduits	3.00d	29-Apr-26 08:00	01-May-26 17:00
A1920	Install Earthing System	2.00d	05-May-26 08:00	06-May-26 17:00
A1930	Install Lightning Protection	2.00d	07-May-26 08:00	08-May-26 17:00
Mechanical		4.00d	12-May-26 08:00	15-May-26 17:00
A1950	Install Electric Heaters	3.00d	12-May-26 08:00	14-May-26 17:00
A1960	Install Ventilation Fans	3.00d	12-May-26 08:00	14-May-26 17:00
A1970	Mechanical First Fix Testing	1.00d	15-May-26 08:00	15-May-26 17:00
Hydraulic		10.00d	18-May-26 08:00	01-Jun-26 17:00
A2000	Hydraulic Testing and Commissioning	3.00d	28-May-26 08:00	01-Jun-26 17:00
A1990	Install Sprinkler Heads	2.00d	26-May-26 08:00	27-May-26 17:00
A1980	Install Sprinkler Pipework	5.00d	18-May-26 08:00	22-May-26 17:00
Second Fix		12.00d	16-Jun-26 08:00	01-Jul-26 17:00
Electrical		12.00d	16-Jun-26 08:00	01-Jul-26 17:00
A2040	Fire alarm and PA/AVWing	4.00d	19-Jun-26 08:00	24-Jun-26 17:00
A2030	Install CCTV and access control	5.00d	19-Jun-26 08:00	25-Jun-26 17:00
A2010	Install lighting fittings	5.00d	16-Jun-26 08:00	22-Jun-26 17:00
A2020	Install small power outlets	3.00d	16-Jun-26 08:00	18-Jun-26 17:00
A2050	Second fix testing	2.00d	26-Jun-26 08:00	29-Jun-26 17:00
A2060	Test and comission all M&E systems	2.00d	30-Jun-26 08:00	01-Jul-26 17:00
Lift, Elevator and Conveyor Installations		10.00d	02-Jul-26 08:00	15-Jul-26 17:00
A1530	Install Kone Monospace® lift in Eastern Frame	10.00d	02-Jul-26 08:00	15-Jul-26 17:00
A1550	Install Kone Mobile Hoist A® lift to existing building	10.00d	02-Jul-26 08:00	15-Jul-26 17:00
External Works		40.00d	25-Jun-26 08:00	19-Aug-26 17:00
External fixtures		35.00d	25-Jun-26 08:00	12-Aug-26 17:00
A2070	Bridge Comissioning (Opening)	0.00d		30-Jul-26 08:00
A1660	External Doors and Stairs	15.00d	25-Jun-26 08:00	15-Jul-26 17:00
A1670	External landscaping	20.00d	16-Jul-26 08:00	12-Aug-26 17:00
Minor building works and and ancillary buildings		15.00d	30-Jul-26 08:00	19-Aug-26 17:00
A1690	General snagging	15.00d	30-Jul-26 08:00	19-Aug-26 17:00
A1700	Works Complete	0.00d		19-Aug-26 17:00
RIBA Stage 6 - Post Construction Phase		45.00d	20-Aug-26 08:00	22-Oct-26 17:00
A1710	CML/Cummins joint handover/Quality Check	5.00d	20-Aug-26 08:00	26-Aug-26 17:00
A1720	Complete QA file	20.00d	27-Aug-26 08:00	24-Sep-26 17:00
A1760	End of Project Life Cycle/RIBA stage 7	0.00d		22-Oct-26 17:00
A1750	QA File Accepted	0.00d		22-Oct-26 17:00
A1740	QA File Approval Period	20.00d	25-Sep-26 08:00	22-Oct-26 17:00
A1730	Submit QA File	0.00d		24-Sep-26 17:00

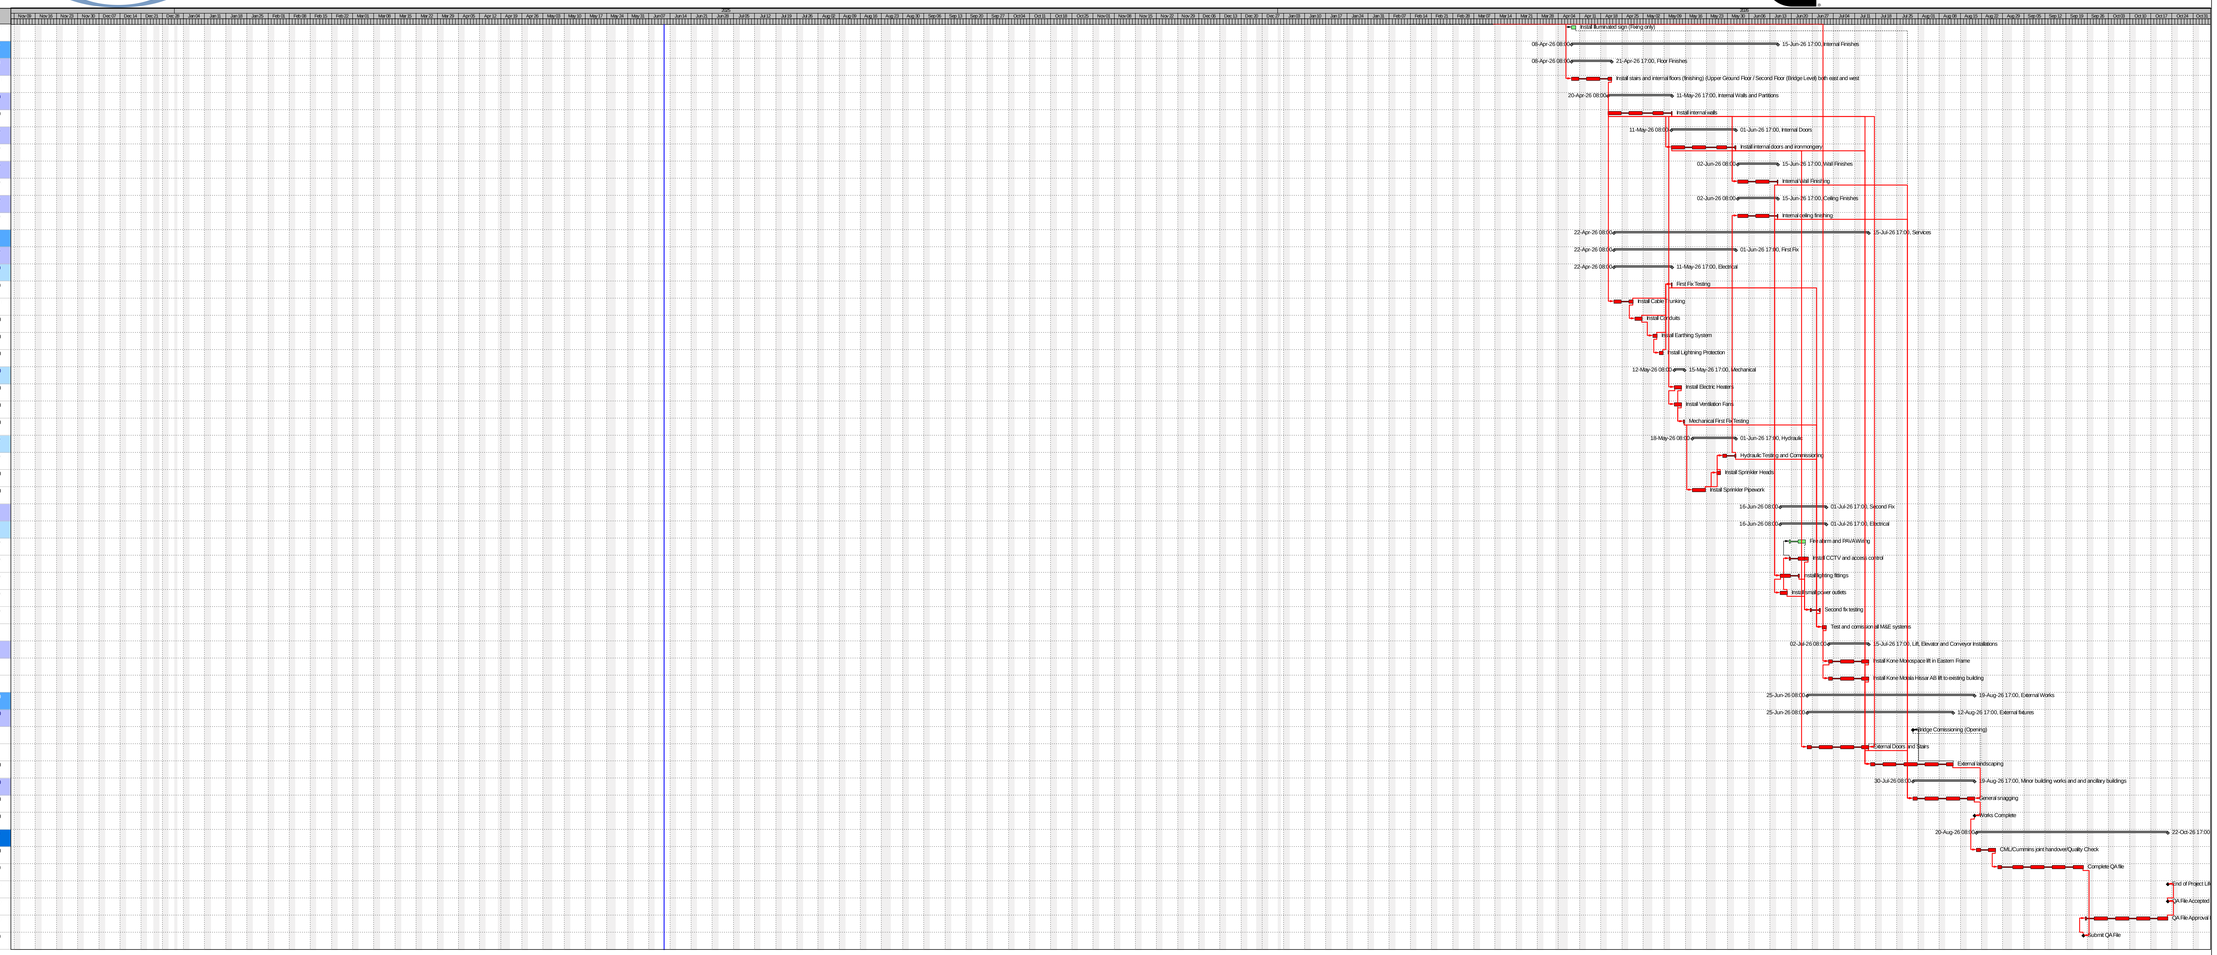

Summary
Milestone
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation
